


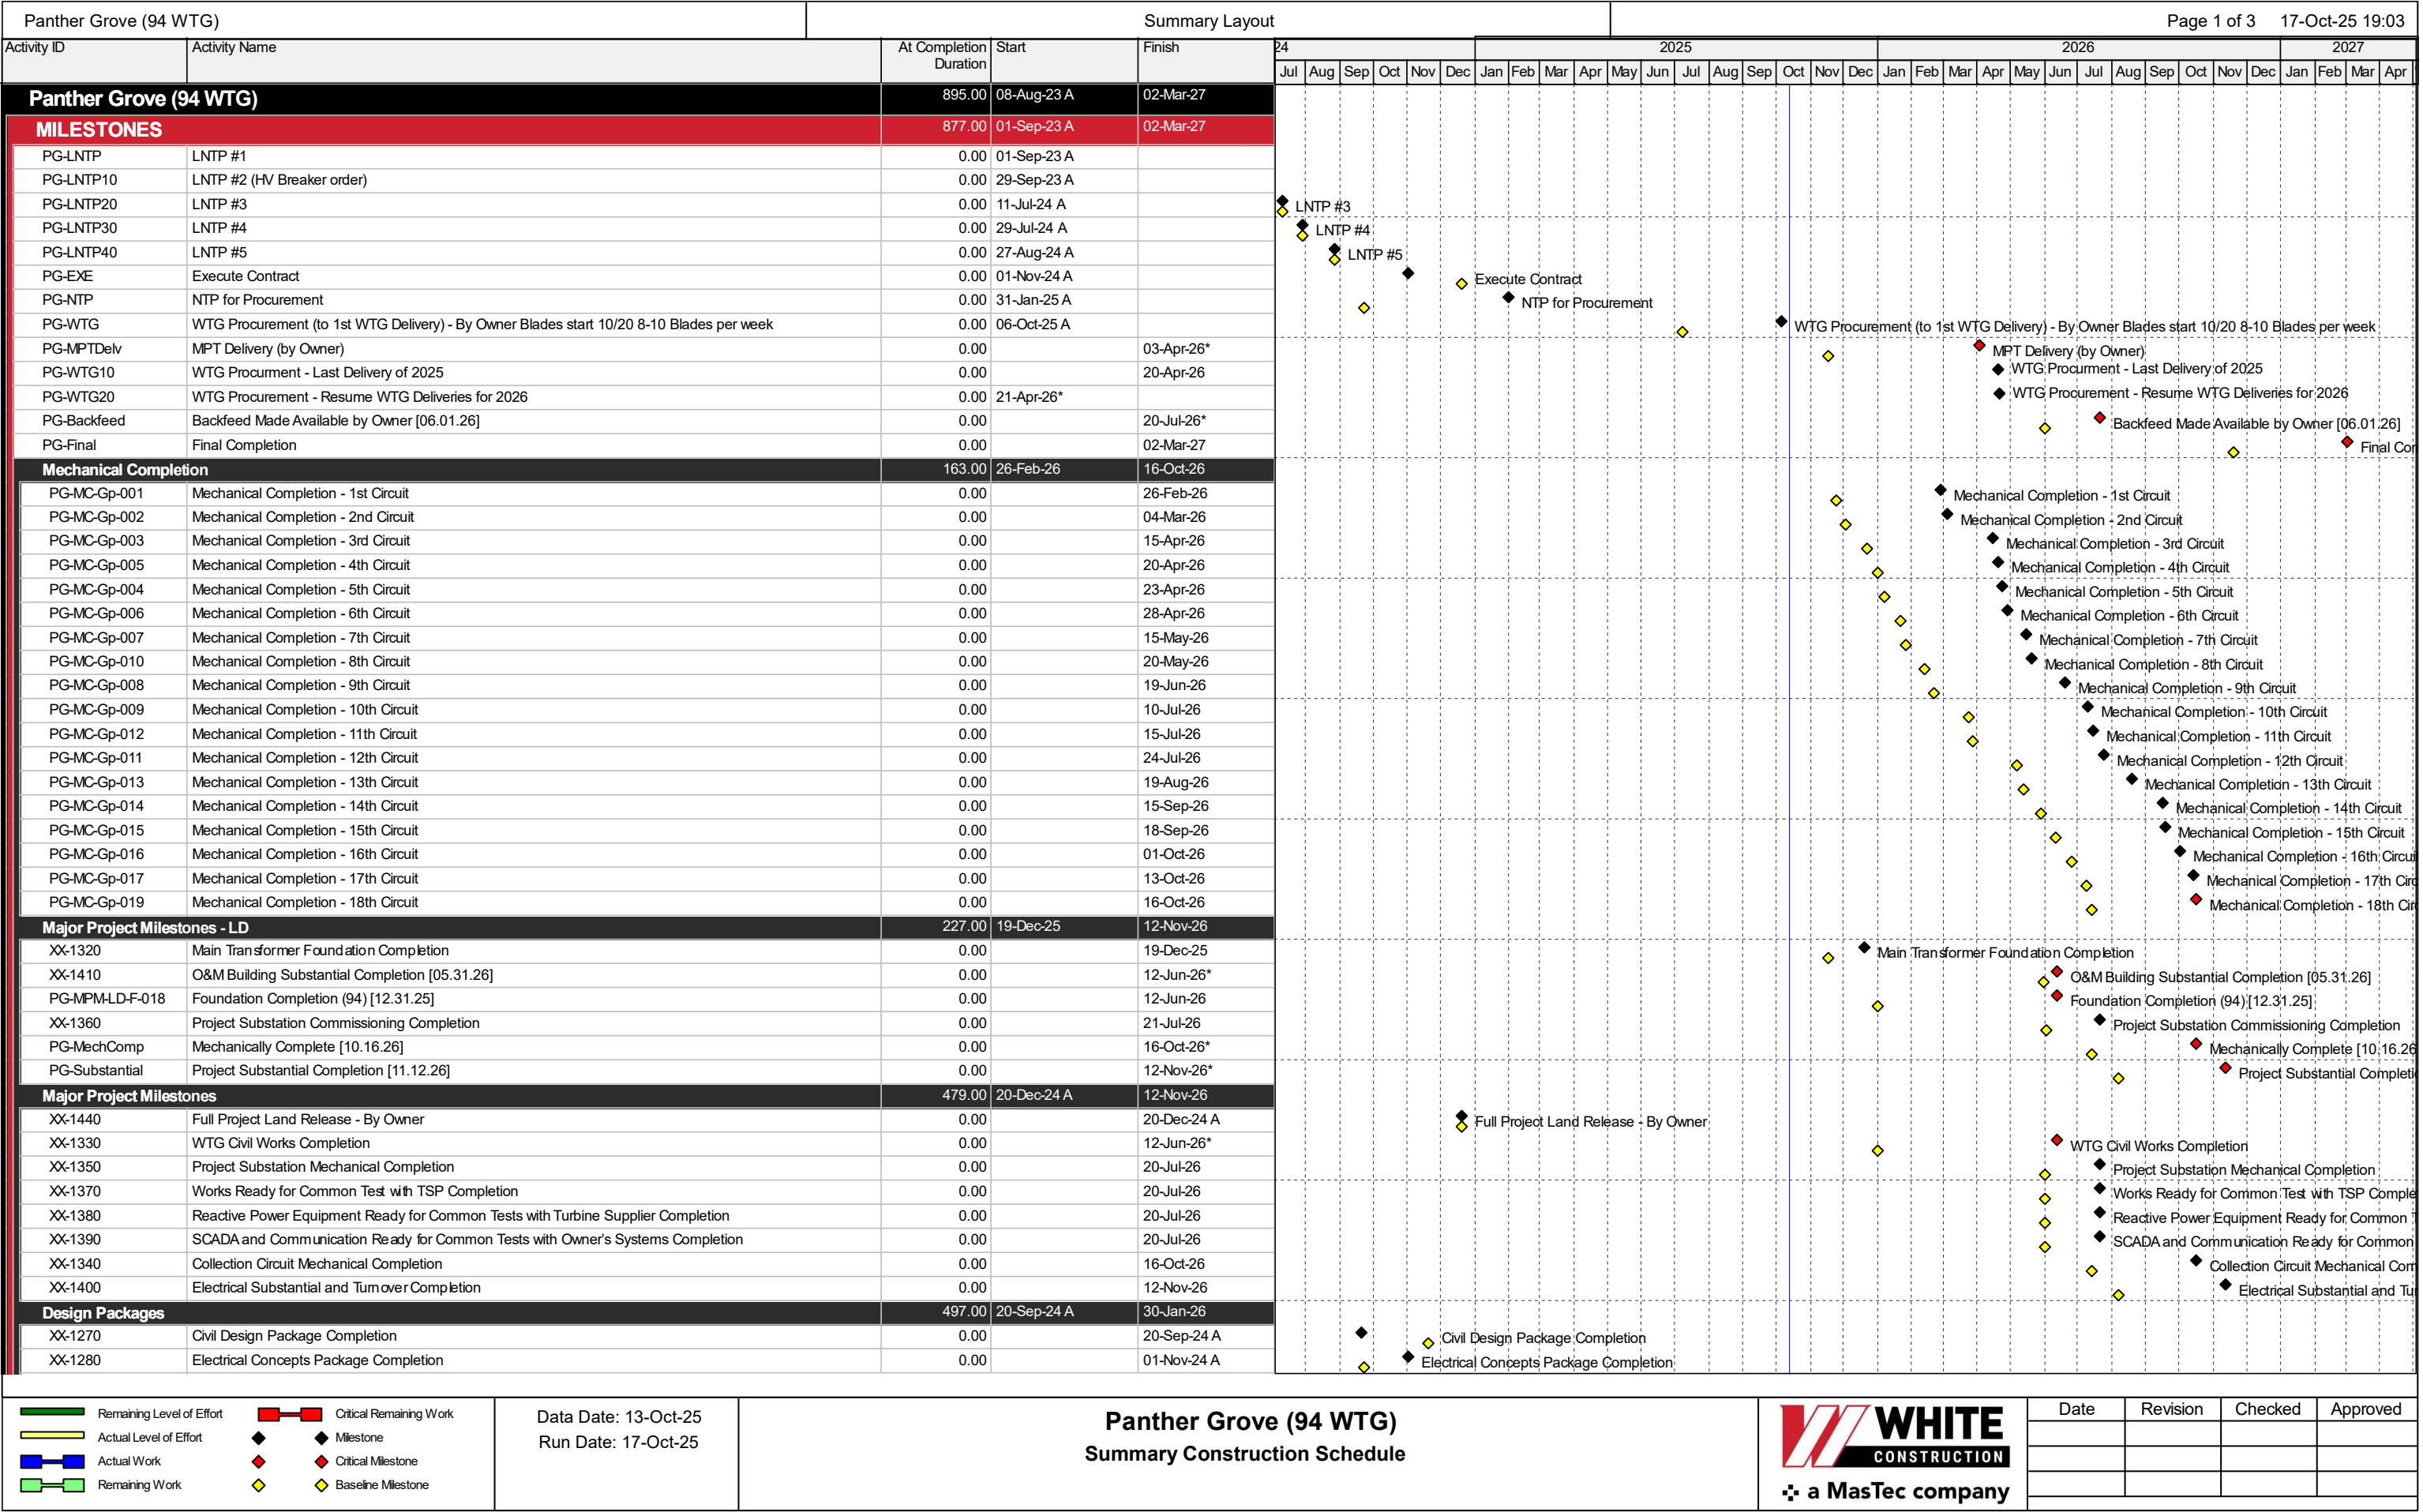

Panther Grove (94 WTG)			Summary Layout												Page 2 of 3 17-Oct-25 19:03																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
Activity ID	Activity Name	At Completion Duration	Start	Finish	24												2025												2026												2027																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
XX-1290	Design Submission for Third Parties' Review Completion	0.00		30-Jan-26*																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																												

Panther Grove (94 WTG)			Summary Layout												Page 3 of 3 17-Oct-25 19:03																								
Activity ID	Activity Name	At Completion Duration	Start	Finish	24	2025												2026												2027									
					Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
Remaining Foundations		135.00	28-May-25 A	09-Dec-25																																			
Strip Foundations		98.00	28-May-25 A	15-Oct-25																																			
Excavate Foundation		110.00	31-May-25 A	05-Nov-25																																			
Pour Mud Mat		118.00	02-Jun-25 A	17-Nov-25																																			
Rebar & Anchor Bolts		117.00	16-Jun-25 A	02-Dec-25																																			
Grounding & Conduit		104.00	01-Jul-25 A	26-Nov-25																																			
Set Form		105.00	07-Jul-25 A	03-Dec-25																																			
Pour Concrete Foundations		103.00	10-Jul-25 A	04-Dec-25																																			
Strip Form		95.00	24-Jul-25 A	08-Dec-25																																			
Backfill Foundations		96.00	24-Jul-25 A	09-Dec-25																																			
Foundations Cure Time		435.00	10-Oct-24 A	18-Dec-25																																			
Turbine Laydown/ Crane Pads		182.00	23-Sep-25 A	12-Jun-26																																			
Set Bearing Plates		86.00	10-Sep-25 A	15-Jan-26																																			
Grout		77.00	24-Sep-25 A	16-Jan-26																																			
ERECTION		260.00	01-Oct-25 A	12-Oct-26																																			
WTG Deliveries		98.00	06-Oct-25 A	06-Jul-26																																			
WTG Blade Deliveries		81.00	03-Nov-25	07-Jul-26																																			
Tower Erection		234.00	01-Oct-25 A	03-Sep-26																																			
Set DTA		191.00	01-Oct-25 A	06-Jul-26																																			
Install Base/Mid		206.00	13-Oct-25	06-Aug-26																																			
Nacelle Prep / Hub Prep		209.00	14-Oct-25	12-Aug-26																																			
Erect Upper Mid/Top/Nacelle/Hub/Single Blades		258.00	13-Oct-25	03-Sep-26																																			
Wind Days Main Erection (8104A)		92.00	13-Oct-25	14-Feb-26																																			
Crane 1		219.00	20-Oct-25	27-Jul-26																																			
Crane 2		90.00	18-May-26	03-Sep-26																																			
Mech / Elec Completions		204.00	22-Dec-25	12-Oct-26																																			
Tower Wiring		194.00	22-Dec-25	28-Sep-26																																			
Mech Completion		195.00	29-Dec-25	01-Oct-26																																			
Tower Cleaning		193.00	02-Jan-26	02-Oct-26																																			
Pre-Walk		193.00	05-Jan-26	05-Oct-26																																			
Owner Walkdown		193.00	06-Jan-26	06-Oct-26																																			
Punchlist		195.00	07-Jan-26	09-Oct-26																																			
MCC Executed		193.00	12-Jan-26	12-Oct-26																																			
O&M BUILDING		126.00	26-Nov-25	29-May-26																																			
Substation Construction		224.00	15-Sep-25 A	04-Aug-26																																			
Civil Work		128.00	15-Sep-25 A	19-Mar-26																																			
Substation Site Work		190.00	15-Sep-25 A	16-Jun-26																																			
Install Foundations		48.00	13-Oct-25	19-Dec-25																																			
Substation Equipment Install / Bus Work		130.00	02-Feb-26	04-Aug-26																																			
Testing & Commissioning		27.00	15-Jun-26	22-Jul-26																																			
MET Tower		297.00	12-May-25 A	15-Jul-26																																			
Engineering & Design		157.00	12-May-25 A	23-Dec-25																																			
Procurement		90.00	10-Dec-25	20-Apr-26																																			
Construction		60.00	21-Apr-26	15-Jul-26																																			
ADLS		334.00	12-May-25 A	04-Sep-26																																			
Engineering & Design		142.00	12-May-25 A	02-Dec-25																																			
Procurement		225.00	19-Aug-25 A	10-Jul-26																																			
Construction		40.00	13-Jul-26	04-Sep-26																																			
Collector System Construction		362.00	12-May-25 A	16-Oct-26																																			
Collection System Construction		338.00	12-May-25 A	14-Sep-26																																			
Collection System Testing and Commissioning		207.00	23-Dec-25	16-Oct-26																																			
RESTORATIONS		226.00	29-Dec-25	13-Nov-26																		</																	
